

SCREEN & FEATURE SPECIFICATION – EzyPM

This document describes the screens and business logic of the EzyPM Project Management System.

Last updated: 2026-03-25

Author: Nhung Trần Thị Hồng

SYSTEM OVERVIEW

- **Platform:** Web application with responsive support for mobile / tablet
- **Scale:** ~100 staff members, ~20 active projects simultaneously
- **Multi-language:** Vietnamese / English
- **Theme:** Light Mode / Dark Mode (user-switchable)
- **Notifications:** Built-in — users receive alerts when assigned a task, when a deadline is approaching, when a new comment is posted, etc.


ROLES & PERMISSIONS

The system has **3 fixed roles** used to control access to features and screens:

Role	Description
Admin	Full system access; can view all data across the system
PM (Project Manager)	Manages assigned projects
Normal User	Standard staff; can only view data relevant to themselves

Note: System roles are separate from project roles. A staff member can be a Backend Developer on Project A and a QC on Project B — project roles are declared individually during resource allocation.

1. GLOBAL HEADER




The header is present on all screens after login.

1.1. Components

- Logged-in user's name
- Account menu
- **Create New Project** button (*visible to Admin / PM only*)
- Notification icon

1.2. Account Menu

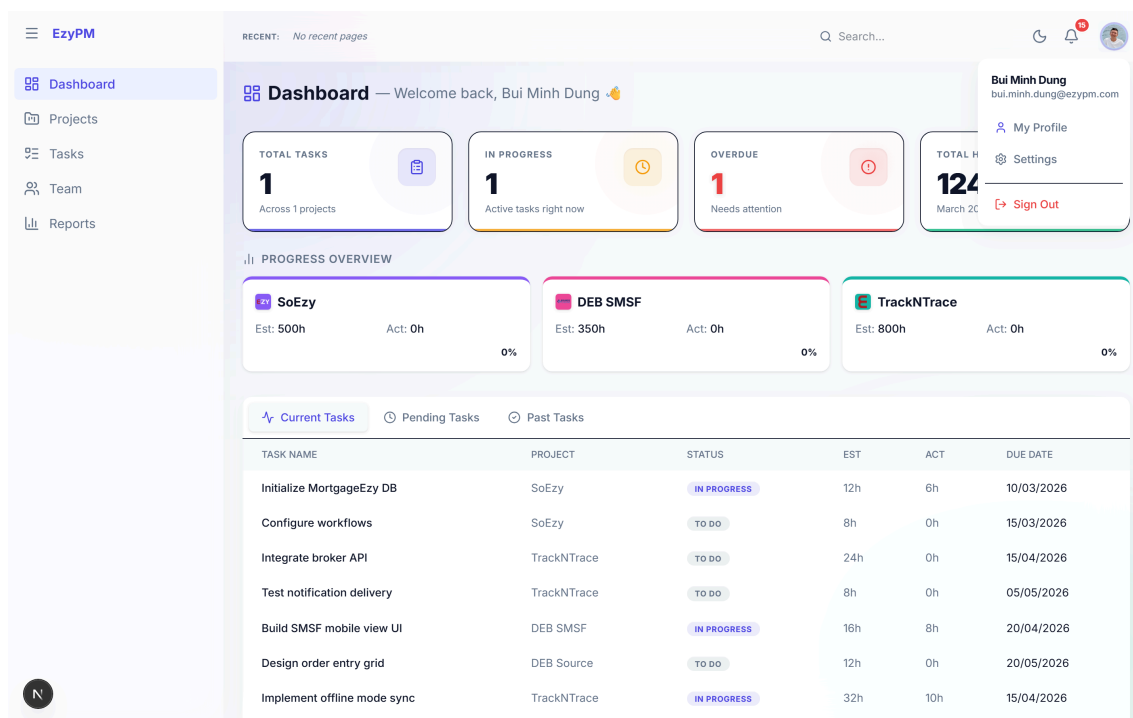


- **My Profile** — Update personal information
- **Change Password** — Update password
- **Switch Theme** — Toggle Light / Dark Mode
- **Log out**

1.3. Create New Project Permission

- Only **Admin** and **PM** can create new projects
- Normal Users do not see or cannot interact with this button

2. DASHBOARD (Personal Overview)

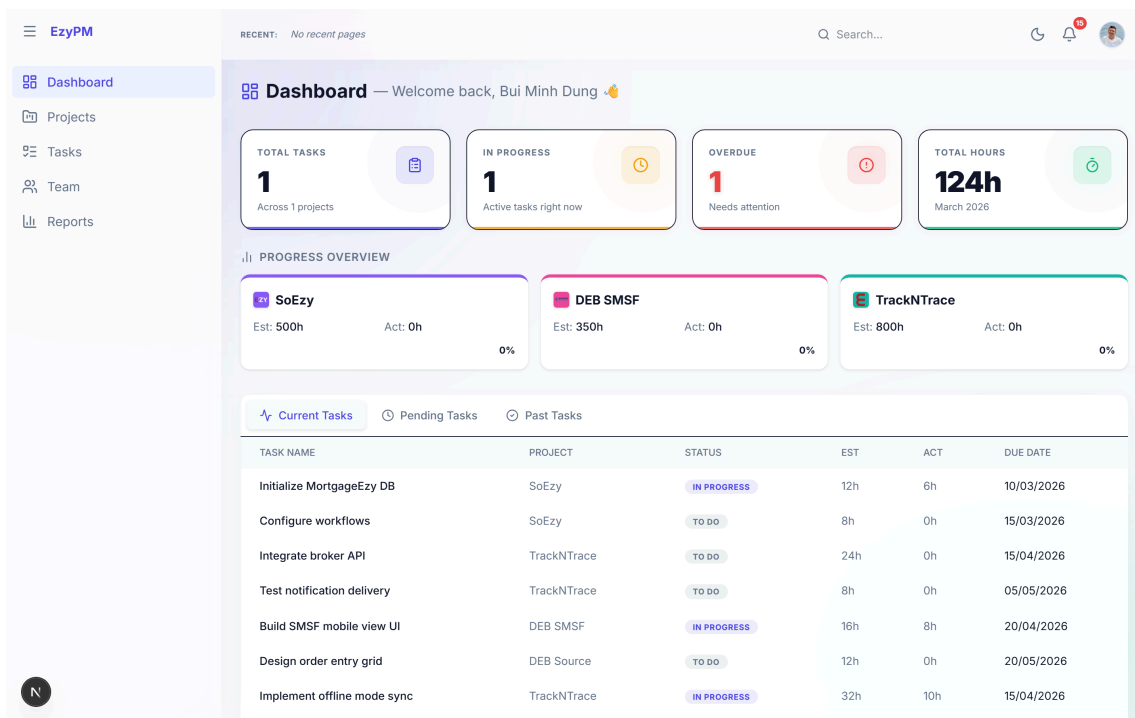

A personal overview screen shown immediately after login. All data is scoped to the currently logged-in user.

2.1. Purpose

Allows staff to quickly check their current workload, task statuses, activity history, and total hours worked.

2.2. Main Components

Task Navigation Tabs

Three horizontal tabs on the same Dashboard page:

- **Current Tasks** — tasks with status = In Progress
- **Pending Tasks** — tasks with status = Pending
- **Past Tasks** — tasks with status = Completed


Each tab shows a freely scrollable table with no row limit.

Progress Overview by Project

Displays each project as an individual **mini-card** (not aggregated). Each card shows:

- Project name
- Progress bar: $\text{Progress (\%)} = \text{Actual Hours} / \text{Estimate Hours} \times 100$
- Total Estimate / Actual / Remaining Hours
- If Actual > Estimate (> 100%): shows the **actual percentage** along with a **warning icon** ⚠

Activities Log

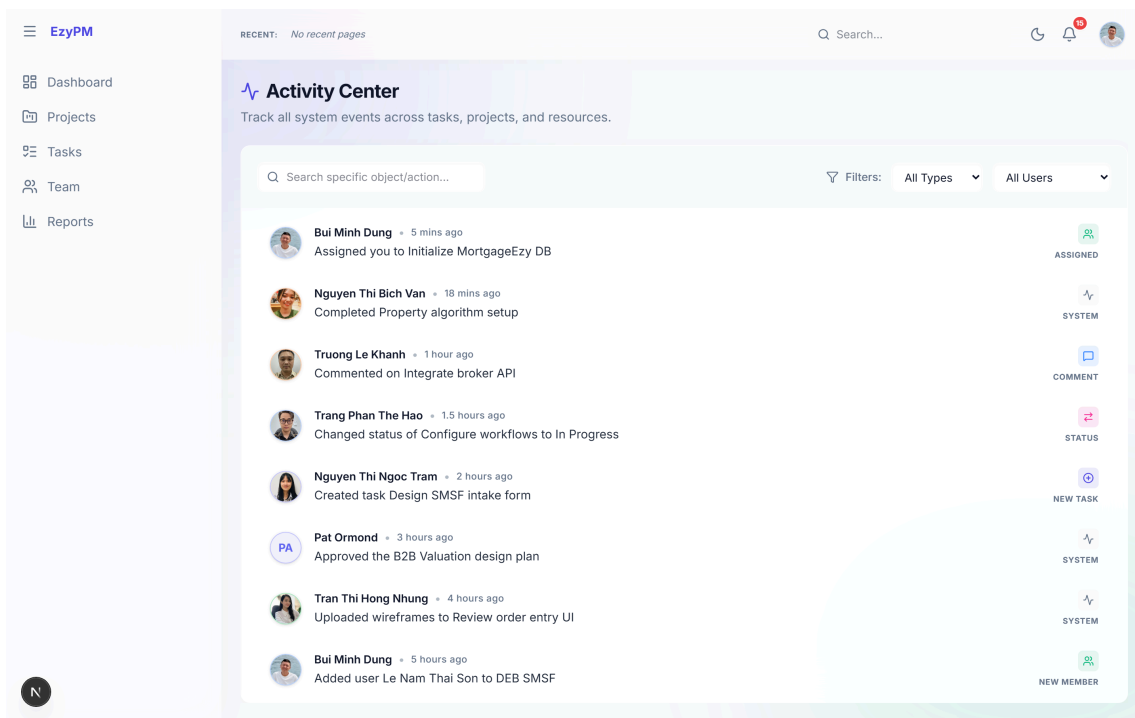


- Automatically recorded by the system, including events such as:
 - Assigned a new task
 - New comment on a task
 - Task completed
 - Task status changed
 - Hours logged
- **Display:** Top 10 most recent notifications; click "View all" to see full history

3. PROJECTS MODULE

Features for managing projects and their tasks.

3.1. Project List

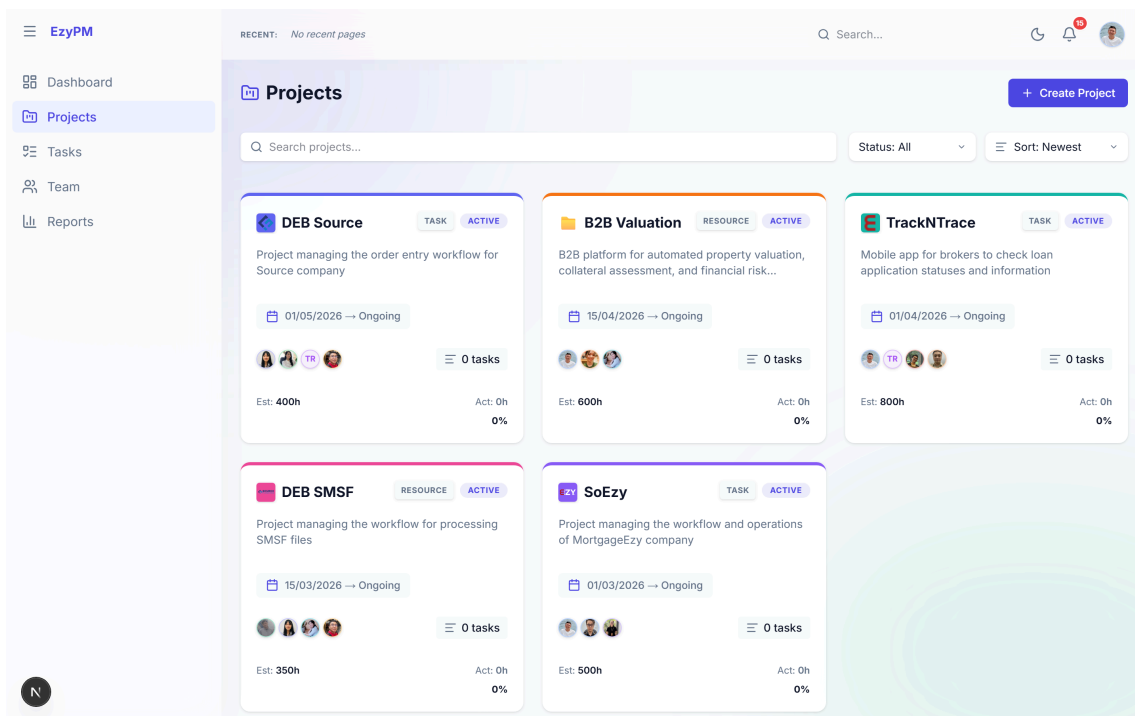

Visibility by role:

- **Admin:** All projects in the system
- **PM:** Projects they manage
- **Normal User:** Projects they are allocated to

Layout: Card grid, infinite scroll when more than 20 projects exist.

Information displayed on each card:

- Project name
- Short description
- Status
- Start date / End date
- EstimateSource (TASK or RESOURCE)
- Number of team members
- Total number of tasks
- Overall progress (Progress %)

3.2. Create / Edit Project

The screenshot shows the EzyPM interface with a sidebar containing 'Dashboard', 'Projects', 'Tasks', 'Team', and 'Reports'. The 'Projects' section is active. A modal titled 'Create New Project' is open, featuring the following fields:

- Project Name ***: Text input with placeholder 'E.g. Website Revamp 2026'.
- Description**: Text area with placeholder 'Brief overview of the project'.
- Avatar URL (optional)**: Text input with placeholder 'https://example.com/logo.png'.
- Estimate Type**: Dropdown menu set to 'Total by Tasks'.
- Initial Estimate (Hours)**: Text input with placeholder 'E.g. 120'.
- Start Date ***: Date input showing '03/25/2026'.
- End Date**: Date input showing 'mm/dd/yyyy'.
- Theme Color**: A row of 12 colored circles, with the 10th circle (purple) selected.

At the bottom of the modal are 'Cancel' and 'Create Project' buttons.

Only **Admin / PM** can create or edit projects. Opens as a **modal**.

Fields:

- Project name (*required*)
- Description
- Status (*required*)
- Start date / End date (*required*)
- **EstimateSource** — select the official estimation method: TASK or RESOURCE (*required*)
- Notes

When editing EstimateSource: a warning message is shown, as this affects Progress and Remaining Hours.


3.3. Project-Level Estimate Hours Logic

Each project has a single active **EstimateSource** at any given time:

EstimateSource	How Project Estimate is Calculated
TASK	Sum of Estimate Hours of all tasks in the project
RESOURCE	Sum of Estimate Hours from resource allocations (e.g. BE 30h + FE 20h + QC 10h + BA 4h)

- **Actual Hours** are always calculated from the total of all logged hours by staff
- **Remaining Hours** = Official Estimate – Actual
- **Progress %** = Actual / Official Estimate × 100

3.4. Project Detail

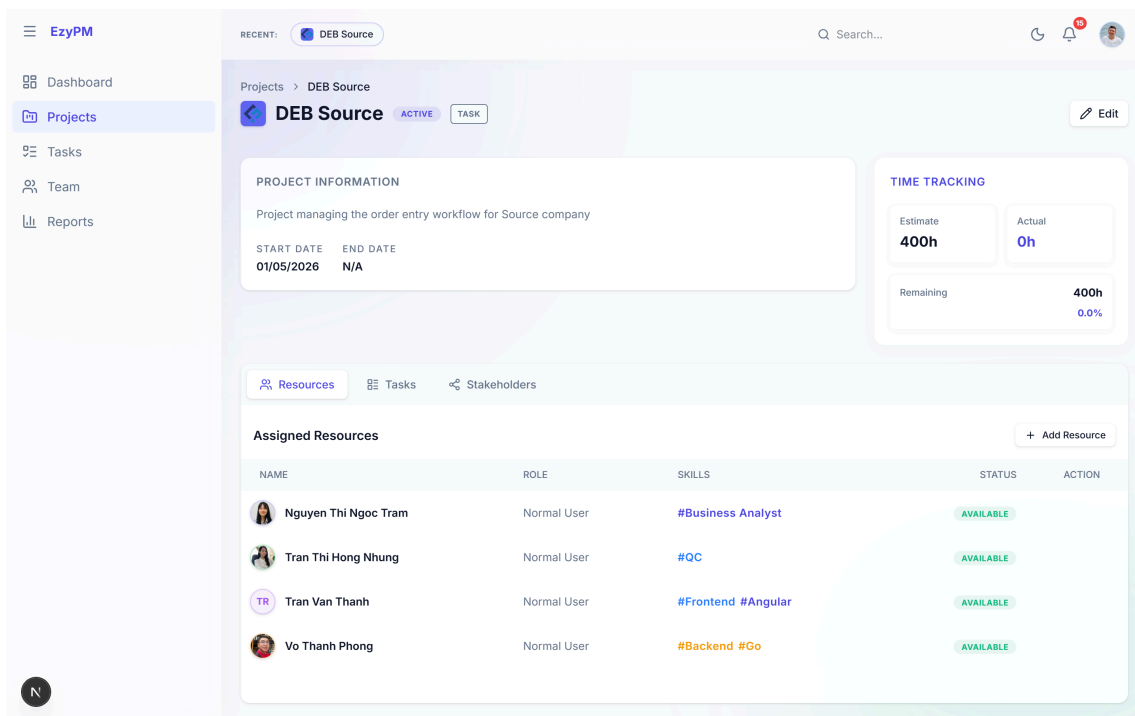

Detail screen for each project. Internal navigation uses **horizontal tabs**.

Overview section (always visible above tabs):

- Name, description, status, dates, EstimateSource
- 4 summary cards: Estimate Hours / Actual Hours / Remaining Hours / Progress %

Tabs:

1. **Resources** — list of staff allocated to the project
2. **Tasks** — task list
3. **Stakeholders** — stakeholder list for the project

3.5. Resource Allocation

Manages assignment of staff to a project. Only **Admin / PM** can add or remove staff.


Fields:

- Select staff member
- Select project role (*flexible per project — free-text combobox with suggested values: Backend, Frontend, QC, BA, etc.*)
- Participation period (start / end date)
- **Estimate Hours per resource** (*only shown when EstimateSource = RESOURCE*)

When a staff member is removed from a project:

- Their assigned tasks **remain unchanged** (not automatically unassigned)
- The removed staff member **can no longer view** those tasks
- Other project members can manually re-assign tasks as needed

3.6. Stakeholder Management

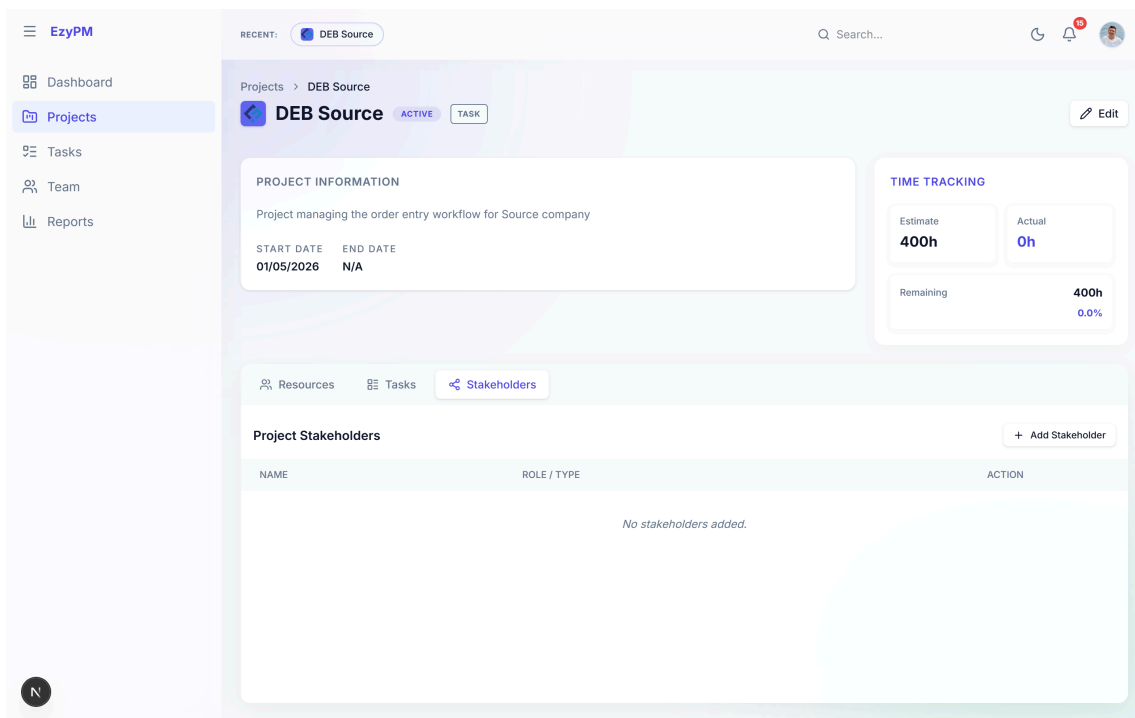

Each project maintains its own stakeholder list, with each stakeholder assigned a role for that project.

System catalogs:

- **Stakeholders** — master list of people / organizations (name, contact info, etc.)
- **Stakeholder Roles** — role catalog (e.g. Client, Vendor, Business Owner, Sponsor, etc.)

Per project:

- Select stakeholders from the system catalog
- Assign a role to each stakeholder within that project
- The same stakeholder can have different roles across different projects

Permissions: Only **Admin / PM** can add, edit, or remove stakeholders in a project.

3.7. Task List

RECENT: No recent pages

Search...

Tasks + Create Task

Search tasks...

Status: All Project: All Assignee: All Priority: All My Tasks

Table Kanban

TASK NAME	PROJECT	ASSIGNEE	PRIORITY	EST / ACT	DUE DATE
IN PROGRESS Initialize MortgageEzy DB	SoEzy	Bui Minh Dung	High	Est: 12h Act: 6h	2026-03-10
TO DO Configure workflows ↳ Subtask	SoEzy	Trang Phan The...	Medium	Est: 8h Act: 0h	2026-03-15
PENDING Design SMSF intake form	DEB SMSF	Nguyen Thi Ngo...	High	Est: 16h Act: 0h	2026-03-25
TO DO Integrate broker API	TrackNTrace	Truong Le Khanh	Critical	Est: 24h Act: 0h	2026-04-15
COMPLETED Property algorithm setup	B2B Valuation	Nguyen Thi Bic...	High	Est: 40h Act: 40h	2026-04-30
ON HOLD Review order entry UI	DEB Source	Tran Thi Hong ...	Medium	Est: 8h Act: 2h	2026-05-10
TO DO Test notification delivery	TrackNTrace	Dao Cam Thanh	Medium	Est: 8h Act: 0h	2026-05-05
IN PROGRESS Build SMSF mobile view UI	DEB SMSF	Le Nam Thai Son	Medium	Est: 16h Act: 8h	2026-04-20
PENDING API Gateway setup	SoEzy	Le Ngoc Minh	High	Est: 24h Act: 0h	2026-05-15
TO DO Design order entry grid	DEB Source	Le Vi	Low	Est: 12h Act: 0h	2026-05-20

Displays all tasks in a project. Users can toggle between **two views**:

Table / List View

- Flat list, not grouped by status
- Filters: Status, Assignee, Priority, Date range
- Subtasks appear as regular tasks in the table (no indentation)

Kanban Board View

- 7 columns corresponding to each status: To Do / In Progress / Pending / On Hold / No Specs / Completed / Closed
- Task cards can be dragged and dropped between columns to change status
- No additional grouping needed — each column represents one status

Columns displayed per task (Table view): Task name, Assignee, Status, Priority, Estimate, Actual, Remaining, Start/End Date

3.8. Create / Edit Task

Opens as a **modal**. All project members can create tasks for projects they belong to.

Fields:

- Task name (*required*)
- Description
- Project (*Normal Users can only select projects they belong to*)
- Assignee (*one person only; staff can self-assign, or PM assigns*)
- Status (*default: To Do*)
- Priority (*required*)
- Estimate Hours
- Start Date / End Date

- Subtasks & Task Links (Blocks / Blocked by / Duplicates / Duplicated by)

Actual Hours are **not entered here** — they are accumulated through the Log Hours mechanism. Remaining Hours is auto-calculated = Estimate – Actual.

Task Status — Lifecycle:

Status	Meaning
To Do	Created, not yet started
In Progress	Currently being worked on
Pending	Waiting — for processing or for a response
On Hold	Temporarily paused
No Specs	Waiting for clear documentation / requirements
Completed	Done
Closed	Closed — no further tracking needed

Any project member can change a task's status to any value — there is no locked workflow.

3.9. Task Detail

The screenshot shows the EzyPM interface for a task titled "Initialize MortgageEzy DB". The task is in the "IN PROGRESS" status with a "High Priority" badge. The description is "Design initial PostgreSQL schema and run migrations".

File Attachments: A file named "specs_v2.pdf" (2.4 MB) is attached.

Subtasks:

- ☒ Design wireframes (Assigned to VAN A)
- ☐ Implement React components (Assigned to VAN A)

Task Links: A link labeled "BLOCKS" points to "Task Beta".

Right Sidebar Information:

- ASSIGNEE:** Bui Minh Dung
- PROJECT:** SoEzy
- START DATE:** 01/03/2026
- DUE DATE:** 10/03/2026
- TIME TRACKING:**
 - ESTIMATE: 12h
 - ACTUAL: 6h
 - REMAIN: 6h
 - Progress: 50.0%
- TIME HISTORY:** 0 ENTRIES (No time has been logged yet.)

2-column layout: left column for main content, right column as an information sidebar.

Left Column — Main Content:

- Task name, status badge, priority badge

- Description
- **Subtasks:** List of child tasks with completion checkboxes; add new subtasks inline
- **Task Links:** Blocks / Blocked by / Duplicates / Duplicated by
- **File Attachments:** Attach files via upload or drag-and-drop
- **Comment Section:** Rich text editor + chronological comment thread
- **Status History:** Automatically logged by the system
- **Log Time History:** Full history of all logged hours

Right Column — Sidebar:

- Assignee (with "Claim task" button if unassigned)
- Project
- Start Date / End Date
- Estimate Hours / Actual Hours / Remaining Hours
- Progress bar (with ⚠ warning if > 100%)
- **"Change Status"** dropdown (7 statuses)
- **"Log Hours"** button

3.10. Log Hours Mechanism

Clicking **"Log Hours"** on the Task Detail opens a modal with:

- **Time (h:mm)** (*required*)
- **Date** (*defaults to today*)
- **Comment / Note** for this log entry

Logic:

- Task Actual Hours = **cumulative sum of all log entries**
- Any project member can log hours for any task in the project
- Each log entry is saved to the task's Log Time History (with logger, timestamp, and comment)

3.11. Comments

The comment editor supports:

- **Rich text:** Bold, Italic, Bullet list, text color, hyperlink
- **Mentions:** @username to tag project members
- **File / image attachments** (upload or paste directly)
- **Edit / Delete** your own comments

3.12. Subtasks & Task Links


Tasks support:

- **Subtasks:** Child tasks under a parent task. Subtasks appear as regular tasks in the task list; the parent-child relationship is only visible inside the Task Detail screen
- **Task Links:** Relationships between tasks
 - Blocks / Blocked by
 - Duplicates / Duplicated by

4. TEAM MODULE (Staff Management)

Permission: Only **Admin** can access the Team module.

4.1. Staff List

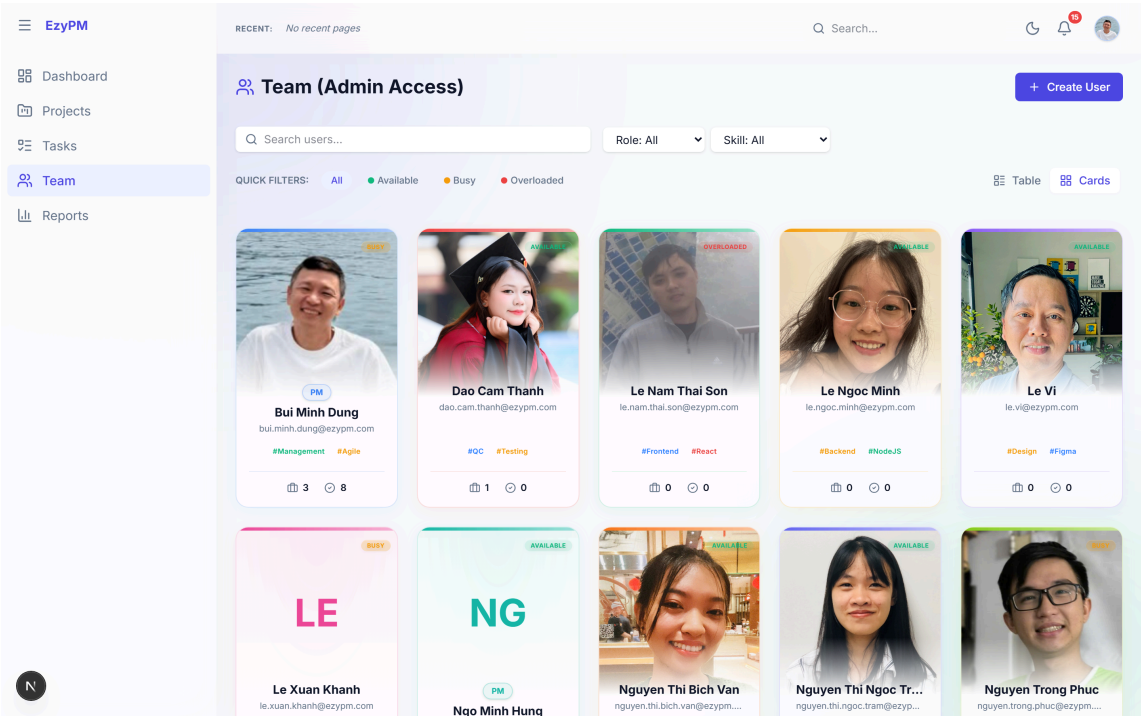

Displays all staff members in the system.

Information displayed:

- Full name + Avatar (initials by default, or uploaded photo)
- System role (Admin / PM / Normal User)
- Skills
- Number of active projects
- Number of active tasks (In Progress + Pending)
- Total hours in charge (sum of Remaining Hours across active tasks)
- **Work status** (auto-calculated — see logic below)

Work Status Logic (auto-calculated):

Status	Condition	Badge Color
Available	No tasks in In Progress or Pending status	● Green
Busy	At least 1 task is In Progress or Pending	● Yellow
Overloaded	Current month Utilization > 100%	● Red

Status is recalculated in real time whenever task data changes.

Quick filter on the staff list:

- Filter by Work Status: Available / Busy / Overloaded
- Admins can use the Available filter to instantly identify who has capacity

Actions available:

- Create new staff member
- Update staff information
- View projects each staff member belongs to

4.2. Staff Detail

The screenshot displays the 'Staff Detail' page for Bui Minh Dung in the EzyPM system. The interface includes a sidebar with navigation options: Dashboard, Projects, Tasks, Team (selected), and Reports. The main content area is titled 'Team > Bui Minh Dung' and features a profile card, performance statistics, participating projects, and active tasks.

Profile Card:

- Name:** Bui Minh Dung
- Email:** bui.minh.dung@ezypm.com
- Role:** PM
- Phone:** —
- Skills:** #Management #Agile

Performance Statistics:

EST. HOURS	ACT. HOURS	RATIO (A/E)	OVERDUE TASKS
12h	6h	0.50x	0

Participating Projects:

- SoEzy (Active)

Active Tasks:

TASK NAME	PROJECT	STATUS	ESTIMATE	ACTUAL
Initialize MortgageEzy DB	SoEzy	IN PROGRESS	12h	6h

Shows the full profile of an individual staff member.

Personal Information:

- Full name, email, phone number
- Avatar: defaults to initials with a fixed random background color; Admin or the staff member can upload a photo
- System role
- Skills (tag-based)

Performance Statistics *(displayed as individual metrics — no single composite score):*

- Total Assigned Tasks
- Completed Tasks
- On-time Completion Rate (%)
- Total Estimate Hours
- Total Actual Hours
- Actual / Estimate Ratio
- Overdue Tasks
- Overrun Tasks

List of active projects (with project role per project)


List of current tasks (In Progress / Pending status)

4.3. Staff Workload View

An aggregated view for Admin to see:

- Which projects each staff member is involved in
- Which tasks they are responsible for (broken down by In Progress / Pending / Completed)
- Current workload per person
- Supports informed resource balancing before assigning new tasks

5. REPORTS MODULE

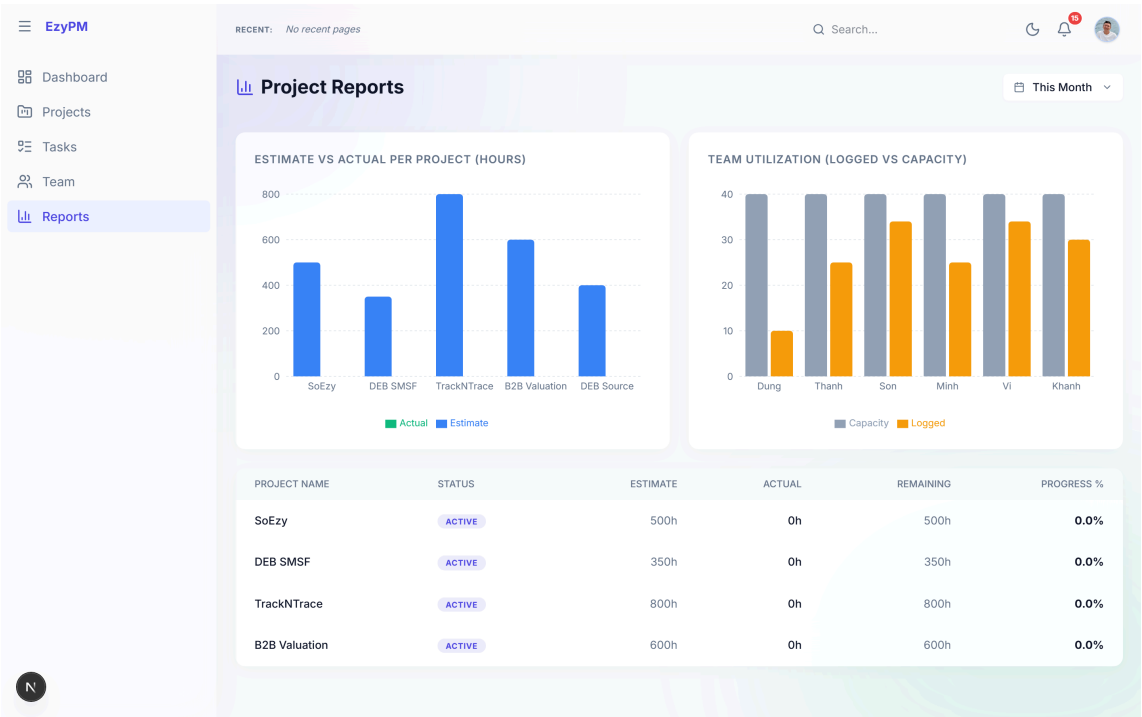

Reporting and analytics features. **View only — no file export supported.**

Common time filter (both options available simultaneously):

- Quick-select dropdown: This Week / This Month / This Quarter / This Year
- Date range picker: custom start and end date

Report visibility by role:

Role	Scope
Admin	All staff, all projects
PM	Staff and projects they manage
Normal User	Their own data only

5.1. Project Report

Chart: Bar chart comparing Estimate vs Actual per project

Data table:

- Project name, status, EstimateSource
- Total Estimate Hours / Actual Hours / Remaining Hours
- Progress (%)
- List of team members
- Task count: Completed / Incomplete / Overdue

5.2. Staff Report

Chart: Bar chart showing Utilization (%) per staff member

Data table:

- Staff name, system role
- Number of projects
- Number of active tasks
- Total Estimate Hours / Actual Hours / Remaining Hours
- **Utilization (%)** = Actual Hours / Standard Working Hours × 100
 - Standard: **8h/day · 5 days/week · 20 days/month**

5.3. Estimate vs. Actual Report

Chart: Line chart showing trends of Estimate vs Actual over time

Data table (filterable by: Project / Task / Staff):

- Estimate Hours
- Actual Hours
- Variance (Actual – Estimate): red ⚠ if positive (over), green if negative (under)
- Variance percentage (%)

5.4. Overdue / Overrun Report

Layout: Color-highlighted table (no chart needed).

Content (4 tabs):

- **Overdue Tasks** — End Date < today, not yet Completed — highlighted red
- **Overdue Projects** — highlighted red
- **Overrun Tasks / Projects** — Actual > Estimate — highlighted orange
- **Overloaded Staff** — Utilization > 100% — highlighted orange

6. SYSTEM CONFIGURATION

System-wide catalogs managed by Admin, used as data sources across all modules.

6.1. Stakeholder Catalog

- Manages the master list of stakeholders across the system
- Fields: Name, email, phone number, organization

EzyPM

Dashboard
Projects
Tasks
Team
Reports
Config

RECENT: No recent pages

Q Search...

System Configuration

Stakeholders Catalog

Stakeholder Roles

Task Statuses

Task Priorities

+ Add Stakeholder

NAME	EMAIL	ORGANIZATION	PHONE	ACTIONS
Pat Ormond	pat.ormond@ezypm.com	EzyPM	-	
Jo Ormond	jo.ormond@ezypm.com	EzyPM	-	
Source Funding	info@sourcefunding.com.au	Source Funding Pty	-	
Alpha Tech Solutions	contact@alphatech.com	-	-	
Valuation DB Provider	api@valuationdb.com	ValDb Inc.	-	

6.2. Stakeholder Role Catalog

- Manages stakeholder role types (Client, Vendor, Business Owner, Sponsor, etc.)
- Admin can add, edit, or delete roles

EzyPM

Dashboard
Projects
Tasks
Team
Reports
Config

RECENT: No recent pages

Q Search...

System Configuration

Stakeholders Catalog

Stakeholder Roles

Task Statuses

Task Priorities

+ Add Role

ROLE NAME	DESCRIPTION	ACTIONS
Client	The customer buying the software or service	
Sponsor	Provides financial backing for the project	
Business Owner	Internal owner or product champion	
Vendor	External supplier of goods or services	
IT Service	Third party technical support or infrastructure	
Partner	Strategic partner co-delivering value	
Other	Uncategorized stakeholder	

6.3. Task Status Catalog

- Manages the workflow statuses available across the platform
- Dynamically syncs with Kanban boards

The screenshot shows the EzyPM System Configuration page. The left sidebar contains a menu with items: Dashboard, Projects, Tasks, Team, Reports, and Config (highlighted). The main content area is titled 'System Configuration' and has a '+ Add Status' button. Below the title, there are tabs for 'Stakeholders Catalog', 'Stakeholder Roles', 'Task Statuses' (selected), and 'Task Priorities'. A table lists the task statuses with columns for Configuration Name, Color, Description, and Actions.

CONFIGURATION NAME	COLOR	DESCRIPTION	ACTIONS
To Do	Grey	Created, not yet started	[Edit] [Delete]
In Progress	Blue	Currently being worked on	[Edit] [Delete]
Pending	Orange	Waiting - for processing or for a response	[Edit] [Delete]
On Hold	Dark Grey	Temporarily paused	[Edit] [Delete]
No Specs	Red	Waiting for clear documentation / requirements	[Edit] [Delete]
Completed	Green	Task is completely done	[Edit] [Delete]
Closed	Light Grey	Closed - no further tracking needed	[Edit] [Delete]

6.4. Task Priority Catalog

- Defines standardized priority levels and their color codes
- Used across Task module for visual identification

The screenshot shows the EzyPM System Configuration page with the 'Task Priorities' tab selected. The table lists the task priorities with columns for Configuration Name, Color, Description, and Actions.

CONFIGURATION NAME	COLOR	DESCRIPTION	ACTIONS
Critical	Red	Must be fixed immediately	[Edit] [Delete]
High	Orange	Important milestone functionality	[Edit] [Delete]
Medium	Blue	Standard priority	[Edit] [Delete]
Low	Dark Grey	Nice to have, non-blocking	[Edit] [Delete]

